



on land into...

# WELL CONSTRUCTION

(UNCONSOLIDATED)

Project 0371 Well MW-15  
 Town/City 26 MILES N. CARLIN  
 County EUREKA State NV  
 Permit No. MO-243 Location MILL 4

Land-Surface Elevation and datum 5408.0 Feet  Surveyed  Estimated  
N2272007 E284636

Installation Date(s) 8/11/90  
 Drilling Method HAMMER  
 Drilling Contractor BECKER DRILLS INC.  
 Drilling Fluid AIR


Development Techniques(s) and Date(s)  
DEVELOPED BY PUMP ON 8/27/90

Fluid Loss During Drilling 38 gals  
 Water Removed During Development 7 gals  
 Static Depth to Water 40.4 ft below M.P.  
 Pumping Depth to Water \_\_\_\_\_ ft below M.P.  
 Pumping Duration \_\_\_\_\_ hours  
 Yield \_\_\_\_\_ gpm

Specific Capacity \_\_\_\_\_ gpm/ft  
 Well Purpose WATER LEVEL MEASUREMENTS AND WATER QUALITY.

Remarks CUTTINGS DAMP FROM 14' Sch. 80 CASING AND SCREEN. 5 1/2 BAGS COL. SILICA #10-20 SAND PACK. NEAT CEMENT GROUT.

Prepared BY P. STELLA

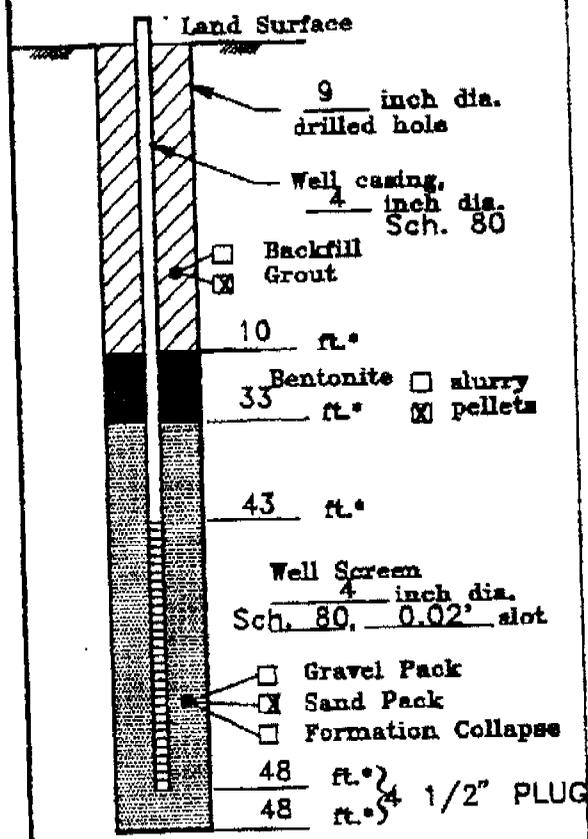

Measuring Point is  
 Top of Well Casing  
 Unless Otherwise Noted.

\*Depth Below Land Surface

3.01' STICK-UP

CLIENT NEWMONT GOLD CO.	PROJECT MILL NO. 4 TAILINGS EXPANSION	TITLE WELL CONSTRUCTION DETAILS OF MW-15
<i>Knight Piessold and Co.</i> CONSULTING ENGINEERS	PROJECT NO 0371	DATE 8/11/90 FIGURE B-4.6
