



# WELL CONSTRUCTION

(UNCONSOLIDATED)

Project 0371 Well MW-16S

Town/City 26 MILES N. CARLIN

County EUREKA State NV

Permit No. MO-243 Location MILL 4

Land-Surface Elevation and datum 5393.1 Feet  Surveyed  
 Estimated  
N2272265 E284292

Installation Date(s) 8/10/90

Drilling Method HAMMER

Drilling Contractor BECKER DRILLS INC.


Drilling Fluid AIR

Development Techniques(s) and Date(s)  
DEVELOPED BY PUMP ON 8/27/90

Fluid Loss During Drilling 10 gals  
 Water Removed During Development      gals  
 Static Depth to Water 40.0 ft below M.P.  
 Pumping Depth to Water      ft below M.P.  
 Pumping Duration      hours  
 Yield      gpm  
 Specific Capacity      gpm/ft  
 Well Purpose WATER LEVEL MEASUREMENTS AND WATER QUALITY.

Remarks CUTTINGS DAMP FROM 5' TO TD. Sch. 80 CASING AND SCREEN. COL. SILICA SAND #10-20 SAND PACK. NEAT CEMENT WITH GROUT. BOREHOLE RESTED 18 HRS S.W.L. AT 38'.

Prepared BY P. STELLA

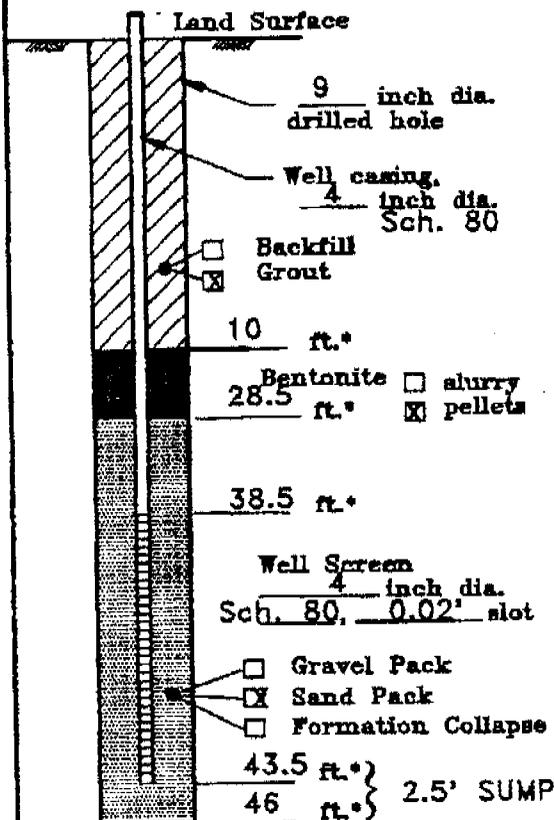

Measuring Point is  
 Top of Well Casing  
 Unless Otherwise Noted.

\*Depth Below Land Surface

2.42' STICK-UP

CLIENT NEWMONT GOLD CO.	PROJECT MILL NO. 4 TAILINGS EXPANSION	TITLE WELL CONSTRUCTION DETAILS OF MW-16S
	PROJECT NO <u>0371</u>	DATE <u>8/11/90</u> FIGURE <u>B-4.7</u>
