

STATE OF NEVADA
DIVISION OF WATER RESOURCES
WELL DRILLER'S REPORT

Well # MFMW-B

OFFICE USE ONLY
Log No. **115753**
Permit No. _____
Basin **228**

PRINT OR TYPE ONLY
DO NOT WRITE ON BACK

Please complete this form in its entirety in accordance with NRS 534.170 and NAC 534.340

NOTICE OF INTENT NO 69356

1. OWNER **Corvus Gold Nevada Inc.** ADDRESS AT WELL LOCATION **1 Boiling Pot Rd**
MAILING ADDRESS **91375 S. Ridgline Blvd. Suite 250** **Beatty, NV 89003**
Highland Ranch, CO 80129 Subdivision Name: _____ County: _____

2. LOCATION NW ¼ NW ¼ Sec 12 T 11 N/SR 46 E Latitude _____ UTM E **519172** NAD 27.
PERMIT/WAIVER No. **M/O -1850** Longitude _____ N **4094680** NAD 83/WGS 84

3. WORKED PERFORMED
 New Well Replace Recondition
 Deepen Other

4. PROPOSED USE
 Domestic Irrigation Test Monitor Stock
 Municipal/Industrial

5. WELL TYPE
 Cable Rotary RVC
 Air Other

6. LITHOLOGIC LOG

Material	Water Strata	From	To	Thick-ness
Debris flow mostly clay brown			25	5
Debris flow lt. Green		25	30	5
Debris flow variegated		30	215	185
Mostly clay white		215	235	20
Debris flow variegated		235	300	65
Debris flow lt. Red		300	315	15
Debris flow variegated		315	405	90
Debris flow lt. Green		405	598	193

9. WELL CONSTRUCTION

Depth Drilled **598** Feet Depth Cased **598** Feet

HOLE DIAMETER (BIT SIZE)

From	To
14 3/4" Inches	0 Feet 20' Feet
8 3/4" Inches	20' Feet 598' Feet

CASING SCHEDULE

Size O.D. (Inches)	Weight/Ft. (Pounds)	Wall Thickness (Inches)	From (Feet)	To (Feet)
10 5/8"		1/4"	0	20'
4 1/2"		1/4"	+2'	598'

Perforations:

Type of perforation	Vertical mill slot
Size of perforation	1/8"
From Blank +2' feet to 498' feet	
From Screen 498' feet to 598' feet	
From _____ feet to _____ feet	
From _____ feet to _____ feet	

Annular Seal: Yes No

Neat Cement 0 to 50' Pumped Poured

Cement Grout _____ to _____ Pumped Poured

Concrete Grout _____ to _____ Pumped Poured

≥30% Bentonite Grout _____ to _____ Pumped Poured

Gravel Pack: Yes No **496 to 598** Pumped Poured
Type: **3/8" gravel**

Bentonite Chips: Yes No **485 to 496** Pumped Poured
Type: **3/8" coated pellets**

7. Water Level

Static water level: **292'** feet below land surface

Artesian Flow: **NA** G.P.M. **NA** P.S.I.

Water Temperature: **Cool** °F

Quality: **Clean**

8. WELL TEST DATA

TEST METHOD: Bailer Pump Air Lift

	G.P.M.	Draw Down (Feet Below Static)	Time (Hours)
At TD.	2		

10. DRILLER'S CERTIFICATION

This well was drilled under my supervision and the report is true to the best of my knowledge.

Name **Boart Longyear Nevada** Contractor

Address **PO Box 2748** Contractor
Elko, NV 89803

Nevada contractor's license number issued by the State Contractor's Board **007086**

Nevada driller's license number issued by the Division of Water Resources, the on-site driller **2330**

Signed *[Signature]*
By driller performing actual drilling on site or contractor

Date **9/13/12**

USE ADDITIONAL SHEETS IF NECESSARY

NOV 05 2012
LAS VEGAS OFFICE
36.999902
-116.784532
NAD 27



North Bullfrog Hills Project - Mayflower Area


Materials			
Well Casing		Units	Amount
Blank*			
	4 inch dia, LCS, Schedule 40, 1/4 inch wall	ft	2800
Screen*			
	4 inch dia, LCS, Schedule 40, 1/4 inch wall	ft	400
	1/8 inch wide FulFlo Louvers,		
Conductor Casing			
Blank			
	10 inch dia, LCS, Schedule 40, 3/16 inch wall	ft	80
Bull Nose cap			
	4 inch dia, LCS, Schedule 40, 1/4 inch wall	items	4
Well Monuments			
Blank			
	8 inch dia, LCS, Schedule 40, 1/4 inch wall	ft	40
	Locking Cap	items	4
*Casing will have welded collars of similar material			
Filter Pack			
Gravel Pack			
	3/8 - to 1/4+ inch SRI Silica Sand gravel pack	ft ³	133.5
Well Seal			
	Neat Cement, surface seal	ft ³	27.3
	Concrete Grout Seal	ft ³	65.4
	3/8 inch Bentonite Hole Plug	ft ³	848.2
VWP Installation			
Datalogger			
	LC-2 w strain relief, one channel, RS-232	items	4
	VWP, unvented, 2 Mpa	items	4
Cable, Blue PVC Cable, 0.250", twisted pairs			
	2- 1,000 ft lengths	ft	2000
	2- 600 ft lengths	ft	1200
	Label1 Cabel Label Charge every 100 ft		

DNR/DWR
RECEIVED

NOV 05 2012

LAS VEGAS OFFICE

MEMW-B
Corvus Gold Nevada, INC.
North Bullfrog Project

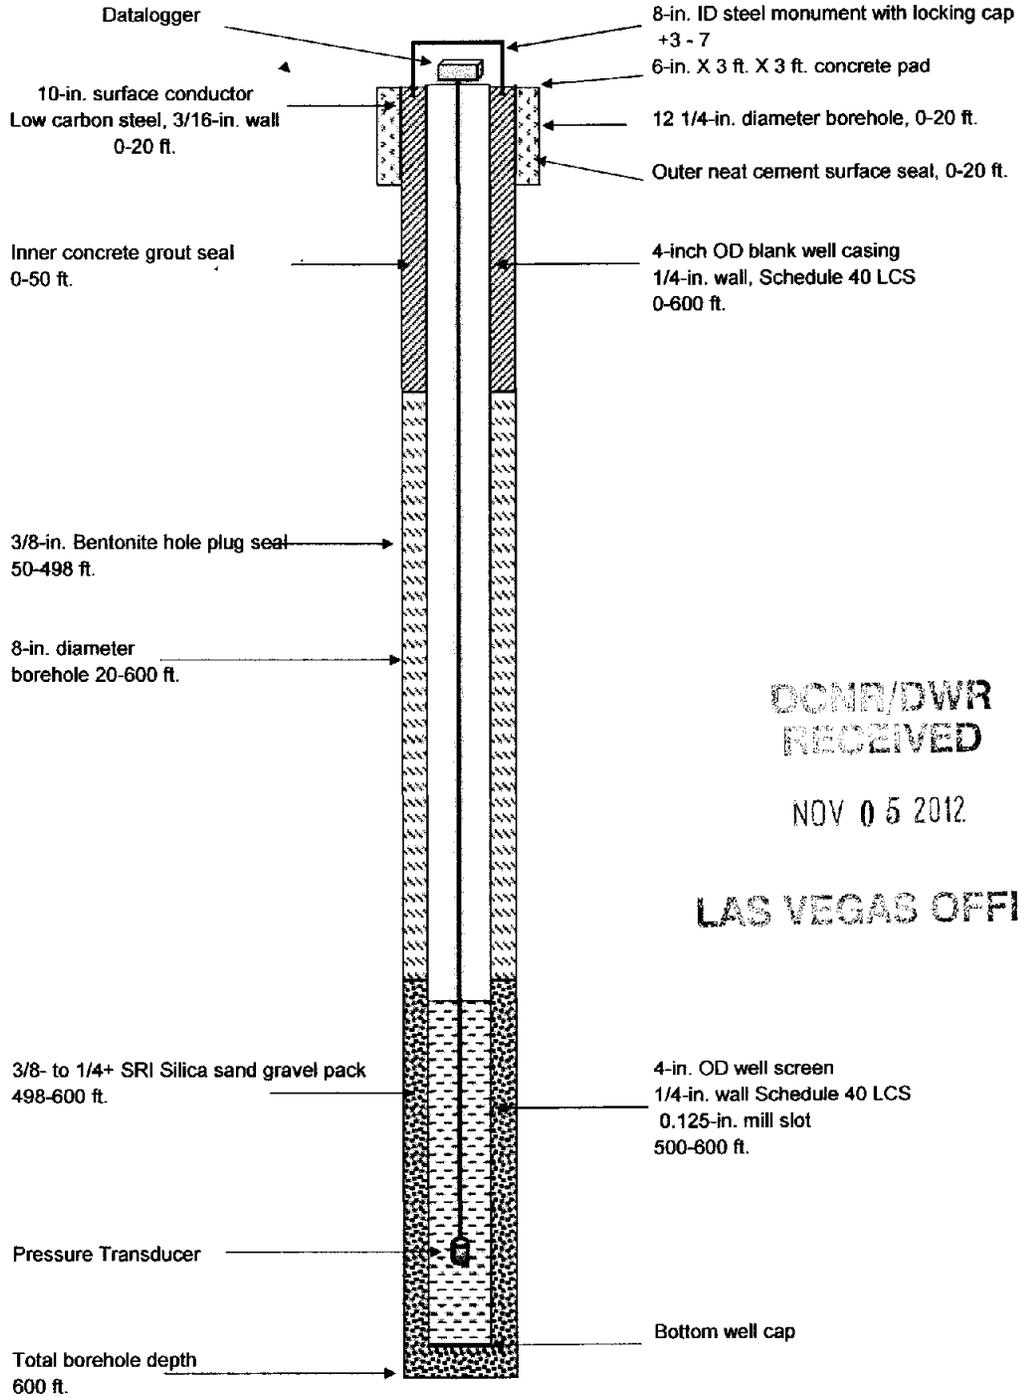

DCNR/DWR
RECEIVED

NOV 05 2012

LAS VEGAS OFFICE

Not to Scale
