STATE OF NEVADA
DIVISION OF WATER RESOURCES
WELL DRILLER'S REPORT

OFFICE USE ONLY
Log No. 22629
Permit No.
Basin 061

PRINT OR TYPE ONLY
DO NOT WRITE ON BACK

Please complete this form in its entirety in accordance with NRS 534.170 and NAC 534.340

WELL# NB-15-08 72795
NOTICE OF INTENT NO. 72794

1. OWNER Barrick Goldstrike
MAILING ADDRESS PO Box 29 Elko, NV 89803
NW
ADDRESS AT WELL LOCATION 27 miles North of Carlin, NV 89822
Subdivision Name: County: Eureka

2. LOCATION NE ¼ SW ¼ Sec 7 T. 36 N S R 50 E
PERMIT/WAIVER No. mo-1996
Issued by Water Resources Parcel No.
Latitude 41.016309 Longitude 116.373501
UTM E N
☒ NAD 27 ☐ NAD 83/WGS 84

3. WORKED PERFORMED
☒ New Well ☐ Replace ☐ Recondition ☐ Deepen ☐ Other

4. INCLINOMETER PROPOSED USE
☐ Domestic ☐ Irrigation ☐ Test ☐ Municipal/Industrial ☐ Monitor ☐ Stock

5. WELL TYPE
☐ Cable ☐ Rotary ☐ RVC ☐ Air ☒ Other Sonic

6. LITHOLOGIC LOG

Material	Water Strata	From	To	Thickness
SEE ATTACHED				

Date started: 5-27, 20 15
Date completed: 5-27, 20 15

9. WELL CONSTRUCTION
Depth Drilled 197 Feet Depth Cased 197 Feet

HOLE DIAMETER (BIT SIZE)

		From		To	
6"	Inches	0	Feet	197	Feet
	Inches		Feet		Feet
	Inches		Feet		Feet

CASING SCHEDULE

Size O.D. (Inches)	Weight/Ft. (Pounds)	Wall Thickness (Inches)	From (Feet)	To (Feet)
3"		PVC Slopeindicator	0	197

Perforations:
Type of perforation NONE
Size of perforation NONE
From feet to feet
From feet to feet
From feet to feet
From feet to feet
From feet to feet

Annular Seal: ☒ Yes ☐ No
☒ Neat Cement 0 to 197 ☒ Pumped ☐ Poured
☐ Cement Grout to ☐ Pumped ☐ Poured
☐ Concrete Grout to ☐ Pumped ☐ Poured
☐ ≥30% Bentonite Grout to ☐ Pumped ☐ Poured
Gravel Pack: ☐ Yes ☒ No to ☐ Pumped ☐ Poured
Type:
Bentonite Chips: ☐ Yes ☒ No to ☐ Pumped ☐ Poured
Type:

7. Water Level
Static water level: feet below land surface
Artesian Flow: G.P.M. P.S.I.
Water Temperature: °F
Quality:

8. WELL TEST DATA
TEST METHOD: ☐ Bailer ☐ Pump ☐ Air Lift

G.P.M.	Draw Down (Feet Below Static)	Time (Hours)

10. DRILLER'S CERTIFICATION
This well was drilled under my supervision and the report is true to the best of my knowledge.
Name Bobart Longyear
Contractor
Address 605 Union Pacific Way Elko, NV 89801
Contractor
Nevada contractor's license number issued by the State Contractor's Board 0021976
Nevada driller's license number issued by the Division of Water Resources, the on-site driller WR-2198
Signed
By driller performing actual drilling on-site or contractor
Date 6/13/2015

(Rev. 05-06)
USE ADDITIONAL SHEETS IF NECESSARY

(NSPO 3-08) (O) 627

CLIENT BGMI DATE 5/24/15

JOB TITLE NBTRF - NW Corner GT Inv. JOB NUMBER 165.008

SUBJECT NB-15-08 General Lithology BY J. Knudsen SHEET 1 OF 1

NB-15-08 General Lithology

0-15	Mine Waste
15-51	Colluvium/Alluvium - Clayey Gravel (GC), Brown clay & silt fines ~~w/ gc~~ with med. plasticity, f-c gr gray, green, and black sub-rounded to sub-angular gravel, some cobbles, saturated below 42'
51-150	Interbedded Sandy Silt (ML) + Silty Clay, brown/red silt (Carlin formation) + brown clay w/ medium plasticity, moist to very moist
150-229	Colluvium/Alluvium - Stiff Clay w/ varying amount of scattered gray, green, and black sub-rounded to sub-angular gravel, moist, most gravel -1" w/ some coarse gravel and cobbles

PURGE WATER, end STATIC - 87'

RECEIVED
2015 JUN 16 PM 2:07
STATE ENGINEERS OFFICE

BOART LONGYEAR
Well Construction Report

Job Name: BARRICK NBTD
Job Number: 111576
Location:

Well Name: HB-15-08
Driller: ROB SALIREY
Helper: AARON OCHOA
Date Installed: Started 5-27-15
Finished 5-27-15

Type of Well:
- [ ] Water Table Observation
- [ ] Piezometer
- [x] Other SLOPE INCIO

A. Height of Well Casing above ground: 2.5 ft.

B. Diameter of Well Casing: 3 in.

C. Surface Seal Bottom: 2 ft.

D. Well Casing: Flush Threaded PVC
- [ ] Schedule 40
- [ ] Schedule 80
- [x] Other

E. Bentonite Seal Top ____ ft.

F. Fine Sand Top ____ ft.

G. Filter Pack Top ____ ft.

H. Screen Joint Top ____ ft.

I. Well Bottom 197 ft.

J. Filter Pack Bottom ____ ft.

K. Borehole Bottom 197 ft.

L. Casing Dia.____ Ft.____
1. To____ From____
2. To____ From____
3. To____ From____
4. To____ From____

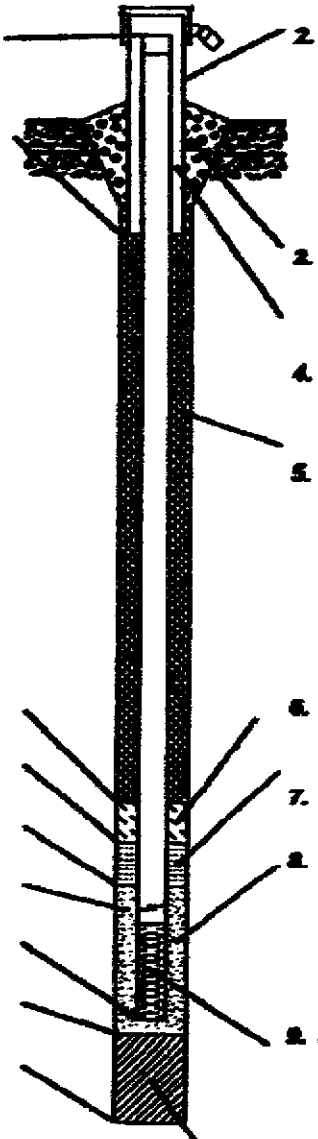

1. Locking Cap? [ ] Yes [ ] No

2. Protective Cover: a. Inside diam. 6 in.
b. Length 5 ft.
c. Material
- [x] Steel
- [ ] Other
d. Bumper Post ____ qty
[ ] 3" [ ] 4"

2. Surface Seal:
- [ ] Bentonite
- [x] Concrete
- [ ] Other

4. Material between Casing and Protop:
- [ ] Bentonite
- [ ] Other

5. Annular Space Seal:
- [ ] Granular Bentonite
- [ ] Bentonite Slurry
- [x] Cement-Bentonite Grout
- [ ] Other

How Installed:
- [ ] Gravity
- [x] Tremie Pumped

6. Bentonite Seal:
- [ ] Granules
- [ ] Pellets

7. Type of Fine Sand:

8. Type of Filter Pack:

9. Screen Material:
Type: ____ Factory Cut ____ Continuous Slot
Slot Size: ____ in.
Length: ____ ft.

10. Backfill Material: (Below filter pack)
- [x] None
- [ ] Other

RECEIVED
2015 JUN 16 PM 2:07
STATE ENGINEER'S OFFICE
