STATE OF NEVADA
DIVISION OF WATER RESOURCES
WELL DRILLER'S REPORT

OFFICE USE ONLY
Log No. 115535
Permit No.
Basin 101

PRINT OR TYPE ONLY
DO NOT WRITE ON BACK

Please complete this form it its entirety in accordance with NRS 534.170 and NAC 534.340

NOTICE OF INTENT NO. 62166

1. OWNER U.S. Navy IW-09
MAILING ADDRESS 4755 Pasture Road Fallon Nv. 89496
ADDRESS AT WELL LOCATION NAS Fallon Nv.
4755 Pasture Road Fallon Nv. 89496

2. LOCATION NW ¼ SE ¼ Sec 23 T 18N N/S R 29 E
PERMIT/WAIVER No. 006-611-01
Issued by Water Resources Parcel No.
Latitude 39.242720 UTM E 2592581.91 ☐ NAD 27
Longitude 118.414984 N 14818838.62 ☑ NAD 83/WGS 84
Subdivision Name: n/a County: Churchill

3. WORKED PERFORMED
☑ New Well ☐ Replace ☐ Recondition
☐ Deepen ☐ Other...

4. X Injection PROPOSED USE
☐ Domestic ☐ Irrigation ☐ Test
☐ Municipal/Industrial ☐ Monitor ☐ Stock

5. WELL TYPE
☐ Cable ☐ Rotary ☐ RVC
☐ Air ☑ Other... auger

6. LITHOLOGIC LOG

Material	Water Strata	From	To	Thickness
Clay,dark brown	no	0	4	4
Silty sand,brown	no	4	9	5
Sandy silt,brown	yes	9	11	2
Clay,brown	no	11	12	1
Silty sand,brown	yes	12	14	2
Clay,brown	no	14	18	4

Date started 5-Feb , 20 12
Date completed 5-Feb , 20 12

7. WELL TEST DATA
TEST METHOD: ☐ Bailer ☐ Pump ☐ Air Lift

G.P.M.	Draw Down (Feet Below Static)	Time (Hours)
	39.407637°N	NAD 27
	118.696013°W	

8. WELL CONSTRUCTION
Depth Drilled 18 Feet Depth Cased 14 Feet

HOLE DIAMETER (BIT SIZE)

	From	To
8 Inches	0 Feet	18 Feet
Inches	Feet	Feet
Inches	Feet	Feet

CASING SCHEDULE

Size O.D. (Inches)	Weight/Ft. (Pounds)	Wall Thickness (Inches)	From (Feet)	To (Feet)
1/2		stainless steel	0	13
1/2		stainless steel	0	8

Perforations:
Type of perforation 1" stainless steel wire wrap
Size of perforation 0.01
From 13 feet to 14 feet
From 8 feet to 9 feet
From feet to feet
From feet to feet
From feet to feet

Surface Seal: ☑ Yes ☐ No
Depth of Seal 7
Placement Method: ☐ Pumped ☑ Poured
Seal Type: ☑ Neat Cement ☐ Cement Grout ☐ Concrete Grout
Gravel Packed: ☑ Yes ☐ No
From 7 feet to 18 feet

9. WATER LEVEL
Static water level n/a feet below land surface
Artesian flow n/a G.P.M n/a P.S.I
Water temperature n/a °F Quality n/a

10. DRILLER'S CERTIFICATION
This well was drilled under my supervision and the report is true to the best of my knowledge.
Name WDC Exploration & Wells (Contractor)
Address PO Box 141 Zamora Ca. 95698 (Contractor)
Nevada contractor's license number issued by the *State Contractor's Board* 0012852
Nevada driller's license number issued by the Division of Water Resources, the *on-site driller* 2111-T1
Signed (By driller performing actual drilling on site or contractor)
Date 3/6/18

RECEIVED 2012 MAR -8 AM 11:25 STATE ENGINEER'S OFFICE

(Rev. 06/10)
USE ADDITIONAL SHEETS IF NECESSARY

Log # 115535

Sheet 1 of 2

TETRA TECH EM INC.

SOIL BORING AND WELL INSTALLATION AND VISUAL CLASSIFICATION LOG

DO:
Bldg./Site:
Project Name:

Boring Number: TT16 - IW09	Date Started: 2/5/12
Drilling Method: (Circle one) HSA Continuous Core/Direct Push/Hand Auger	Date Completed: 2/5/12
Air Rotary/Mud Rotary/Dual Tube Percussion/Sonic/Vacuum	Logged By: V. PRILEPIN
Outer Diameter of Boring: 8"	Drilling Subcontractor: WDC Expl. & Wells
Inner Diameter of Well Casing: 0.5" and 0.5"	Driller: GARY WHITLEY
Depth to Water (ft./bgs.)	Location Sketch:

RECEIVED
2012 MAR -8 AM 11:2
STATE ENGINEERS OFFICE

Time	Depth (ft) bgs	Drive Interval	Recovered Interval	Sample ID	Blow count (per 6 inches) / V.S. utility type, dia.	Description	USCS soil symbol	Well construction	OVM (ppm)
	2		90			0-5 HAND AUGERED 0-0.5 silty sand, brown, loose, dry 0.5-3.5 clay, dark brown, 7.5YR 3/4, low plasticity, tiny mica, medium stiff to stiff, 100% clay	SM CL		
	4					3.5-8.5 silty sand to sand, brown, fine to submedium grained, w/mica up to 1.5mm wet at ~8	SM/SP		
	6		50						5 B.S. 7.5
	8					8.5-10.5 sandy silt to clayey silt, brown, micaceous, wet to saturated (part of interval not retreived); 70% silt	ML		8 9
	10		70						10

Log #115535

Sheet 2 of 2

TETRA TECH EM INC.

SOIL BORING AND WELL INSTALLATION AND VISUAL CLASSIFICATION LOG

TT16-IW09

DO:

Bldg./Site: 16

Project Name: NAS FALLON TCRA

Time	Depth (ft) bgs	Drive Interval	Recovered Interval	Sample ID	Blow count (per 6 inches) / V.S. utility type, dia.	Description	USCS soil symbol	Well construction	OVM (ppm)
	12	70	70			10.5-12, clay, brown, 7.5YR 4/2, soft to medium stiff, medium to low plasticity, w/tiny mica, wet to moist; 100%, grading to silty sand at ~12	ML CL		10 0.5 12
	14					12-14 silty sand to sand, brown, very fine to fine, to submedium grained, saturated, mica up to 2 mm, loose; 70-100% sand, 20 silt, 10 clay	SM		13 14
	16		100			14-18 clay, brown, 7.5YR 4/2, medium soft to med. stiff, low plasticity, crumbles easily, w/tiny mica, thin zones of organic dark gray coloration, 100% clay	CL		14.4
	18					T.D 18			

RECEIVED
2012 MAR 8 AM 11:25
STATE ENGINEERS OFFICE

INJECTION
~~MONITORING~~ WELL COMPLETION RECORD

Log # 115535

TETRATECH EM INC

MONITORING WELL
~~MONITORING~~ WELL NO.: TT16-IW09
PROJECT: NAS FALLON TCRA
SITE: 16
BOREHOLE NO.:
WELL PERMIT NO.:
TOC TO BOTTOM OF WELL:

DRILLING INFORMATION
DRILLING BEGAN:
DATE: 2/5/12 TIME: 9:55
WELL INSTALLATION BEGAN:
DATE: 2/5/12 TIME: 10:25
WELL INSTALLATION FINISHED:
DATE: 2/5/12 TIME: 12:15
DRILLING CO.: WDC
DRILLER: GARY WHITAEY
LICENSE:
DRILL RIG: HSA CME-85
DRILLING METHOD:
- [x] HOLLOW STEM AUGER
- [ ] AIR ROTARY
- [ ] OTHER:

DIAMETER OF AUGERS:
ID: OD: 8"

WELL CASING
- [ ] SCHEDULE 40 PVC
- [x] OTHER:

PRODUCT: SS 316
MFG. BY: APT WATER
CASING DIAMETER
ID: OD: 0.5"
LENGTH OF CASING:

WELL SCREEN
- [ ] SCHEDULE 40 PVC
- [x] OTHER:

PRODUCT: SS 316
MFG. BY: APT WATER
CASING DIAMETER:
ID: OD: 0.5"
SLOT SIZE: 0.01
LENGTH OF SCREEN: 9' (both screens)

BOREHOLE BACKFILL
AMOUNT CALCULATED:
AMOUNT USED:
- [ ] BENTONITE CHIPS, SIZE:
- [x] BENTONITE PELLETS, SIZE: 1/4" Coated
- [ ] SLURRY:
- [x] FORMATION COLLAPSE:
- [ ] OTHER:

PRODUCT:
MFG. BY:
METHOD INSTALLED
- [ ] POURED
- [ ] TREMIE
- [ ] OTHER:

SURFACE COMPLETION
- [x] FLUSH MOUNT
- [ ] ABOVE GROUND WITH BUMPER POST
- [ ] CONCRETE
- [ ] ASPHALT

N

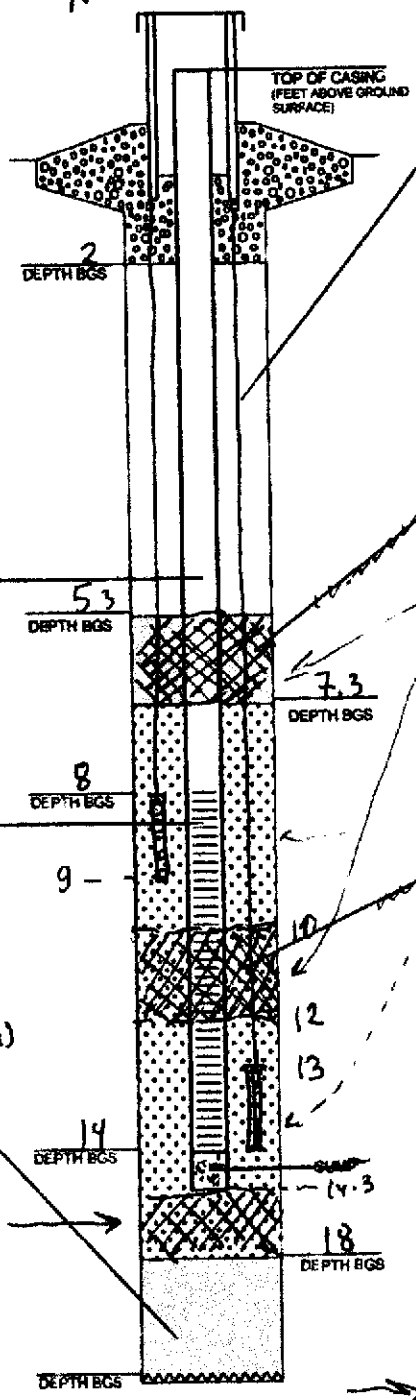

S

SURVEY INFORMATION
TOC ELEVATION:
GROUND SURFACE ELEVATION:
NORTHING:
EASTING:
DATE SURVEYED:
SURVEY CO.:

ANNULAR SEAL
VOLUME CALCULATED:
AMOUNT USED: ~ 1 bag
- [x] GROUT FORMULA (PERCENTAGES)

PORTLAND CEMENT: 95%
BENTONITE: 5%
WATER:
- [ ] PREPARED MIX

PRODUCT:
MFG. BY:
METHOD INSTALLED:
- [x] POURED
- [ ] TREMIE
- [ ] OTHER:

BENTONITE SEAL
VOLUME CALCULATED:
AMOUNT USED: 3 bags in both
- [x] ~~PELLETS, SIZE: 1/4" COATED (lower~~ v.a
- [x] CHIPS, SIZE: MEDIUM (upper) lower
- [ ] OTHER:

PRODUCT: PIREGOLD
MFG. BY: CETCO
METHOD INSTALLED:
- [x] POURED
- [ ] TREMIE
- [ ] OTHER:

AMOUNT OF WATER USED:

FILTER PACK
- [ ] PREPACKED FILTER

VOLUME CALCULATED: 2
AMOUNT USED: 2 bags (lower) 3 bags (upper)
- [x] SAND, SIZE: 2/12

PRODUCT: CEMEX
MFG. BY:
METHOD INSTALLED:
- [x] POURED
- [ ] TREMIE
- [ ] OTHER:

WATER LEVEL:
(BTOC AFTER WELL INSTALLATION)

CENTRALIZERS USED?
- [ ] YES
- [ ] NO

CENTRALIZER DEPTHS:

LEGEND
BGS = BELOW GROUND SURFACE
BTOC = BELOW TOP OF CASING
N/A = NOT APPLICABLE
NR = NOT RECORDED
TOC = TOP OF CASING

RECEIVED 2012 MAR 18 AM 11:25 RECORDS OFFICE
