33764

I

3 ft x 3 ft square

SURFACE GRADE

Subbase fill

Native soil

Native Backfill

Pre-mix concrete & boulder

- Approx. 4 ft

Abandonment data :

Well diameter = 6.5 in
Casing diameter = 10 in
Boring diameter = 12 in

Sacks of cement used = 48

Gallons of cement pumped = 648

Time to fill = 2 hrs

Blank casing interval = 0 - 68 ft

Screen interval = 68 - 108 ft

Water level Estimated = 97 ft

SCHEMATIC L RECOVERY WELL (R-3) ABANDONMENT

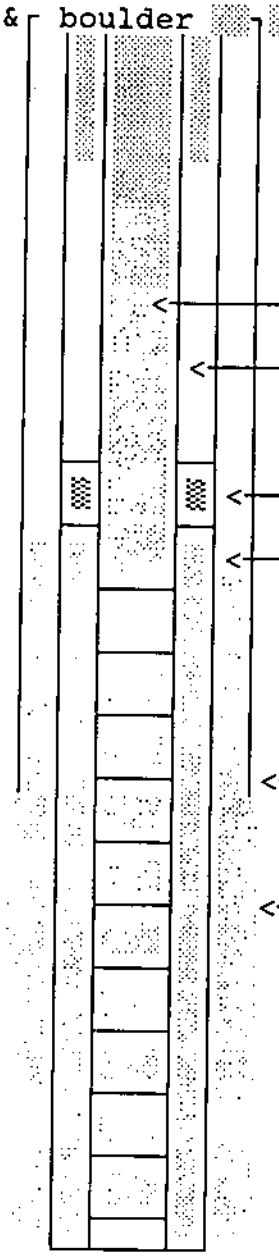

neat cement

sand pack not influenced by cement = 60 ft

bentonite seal= 2 ft

Interval between bentonite and top of 6.5 in screen = 2 ft

10 in. casing to 86ft

Estimated radius of influence of pumped cement = 9in

(no scale)

Total Depth =108 ft

GROUNDWATER TECHNOLOGY, INC.
