STATE OF NEVADA
DIVISION OF WATER RESOURCES
WELL DRILLER'S PLUGGING REPORT

OFFICE USE ONLY
Log No. 120366
Permit No.
Basin 179

PRINT OR TYPE ONLY
DO NOT WRITE ON BACK

Please complete this form in its entirety in accordance with NRS 534.170 and NAC 534.340

NOTICE OF INTENT NO. 65684
WELL NAME (If applicable): MW-4

1 OWNER Reed R-Place Shell
MAILING ADDRESS 909 Avenue E, Ely NV. 89301
ADDRESS AT WELL LOCATION See attached Map.
Subdivision Name: County: White Pine

2 LOCATION NW ¼ NE ¼ Sec 15 T 16 N/S R 63 E
PERMIT/WAIVER No. 6-000198/6-000196
Issued by Water Resources Parcel No.
Latitude 39.25584°
Longitude 114.86897°
UTM E ☐ NAD 27
N ☒ NAD 83/WGS 8

3 TYPE OF WELL
☐ Domestic ☐ Irrigation ☐ Test
☐ Municipal/Industrial ☒ Monitor ☐ Stock
Is this well being plugged because a replacement well was drilled? no
If yes, what is replacement well NOI?
Is there an existing well log?
If yes, what is NDWR well log #?

4 EXISTING WELL CONSTRUCTION
Depth Drilled 85 Feet Depth Cased 85 Feet

EXISTING CASING SCHEDULE

Size O.D. (Inches)	Weight/Ft. (Pounds)	Wall Thickness (Inches)	From (Feet)	To (Feet)
2	PVC	Sch 40	0	85

Existing Perforations:
Type of perforation
Size of perforation
From 60 feet to 85 feet
From feet to feet
From feet to feet
From feet to feet
From feet to feet

5 WATER LEVEL
Static water level 65' feet below land surface
Artesian flow G.P.M. P.S.I
Water temperature °F Quality

6 Additional Notes or Comments
Trimmie Grouted neat Cemment from bottom of well to 1' Below ground Surface. Then Concrete Traffic Vault in place.

plugs unknown log
nad27
39.25590°N
114.86811°W

7 WELL PLUGGING PROCEDURE
Was well cleaned out to total depth? ☒ yes ☐ no
If well was not cleaned out to total depth, please explain why:
Was the well contaminated? ☐ yes ☒ no
Was the casing pulled? ☐ yes ☒ no If pulled from: feet to feet
Was the casing over drilled? ☐ yes ☒ no
If casing was left in place, please show where additional perforations were made:
Additional Perforations.
Type of perforater used: ~~N/A~~ None
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot
From feet to feet Number of perfs per linear foot

2014 JUN 16 PM 1:24

8 WELL PLUGGING MATERIALS
Material Used
From 0 feet to 85 feet Neat Cemment ☒ Pumped ☐ Poured
From feet to feet ☐ Pumped ☐ Poured
From feet to feet ☐ Pumped ☐ Poured
From feet to feet ☐ Pumped ☐ Poured
From feet to feet ☐ Pumped ☐ Poured
From feet to feet ☐ Pumped ☐ Poured
Neat Cement Fluid Weight 14.5 lbs/gal
Bentonite Grout % bentonite
Date Started 5/14/14
Date Completed 5/14/14

9 DRILLER'S CERTIFICATION
This well was plugged and abandoned under my supervision and the report is true to the best of my knowledge.
Name Haz-Tech Drilling Inc.
Contractor
Address PO Box 940
Contractor
Meridian ID. 83680
Nevada contractor's license number issued by the State Contractor's Board 0038018
Nevada driller's license number issued by the Division of Water Resources, the on-site driller M-2246
Signed Jason Adams
By driller performing actual drilling on site or contractor
Date 5/18/14

log 120366

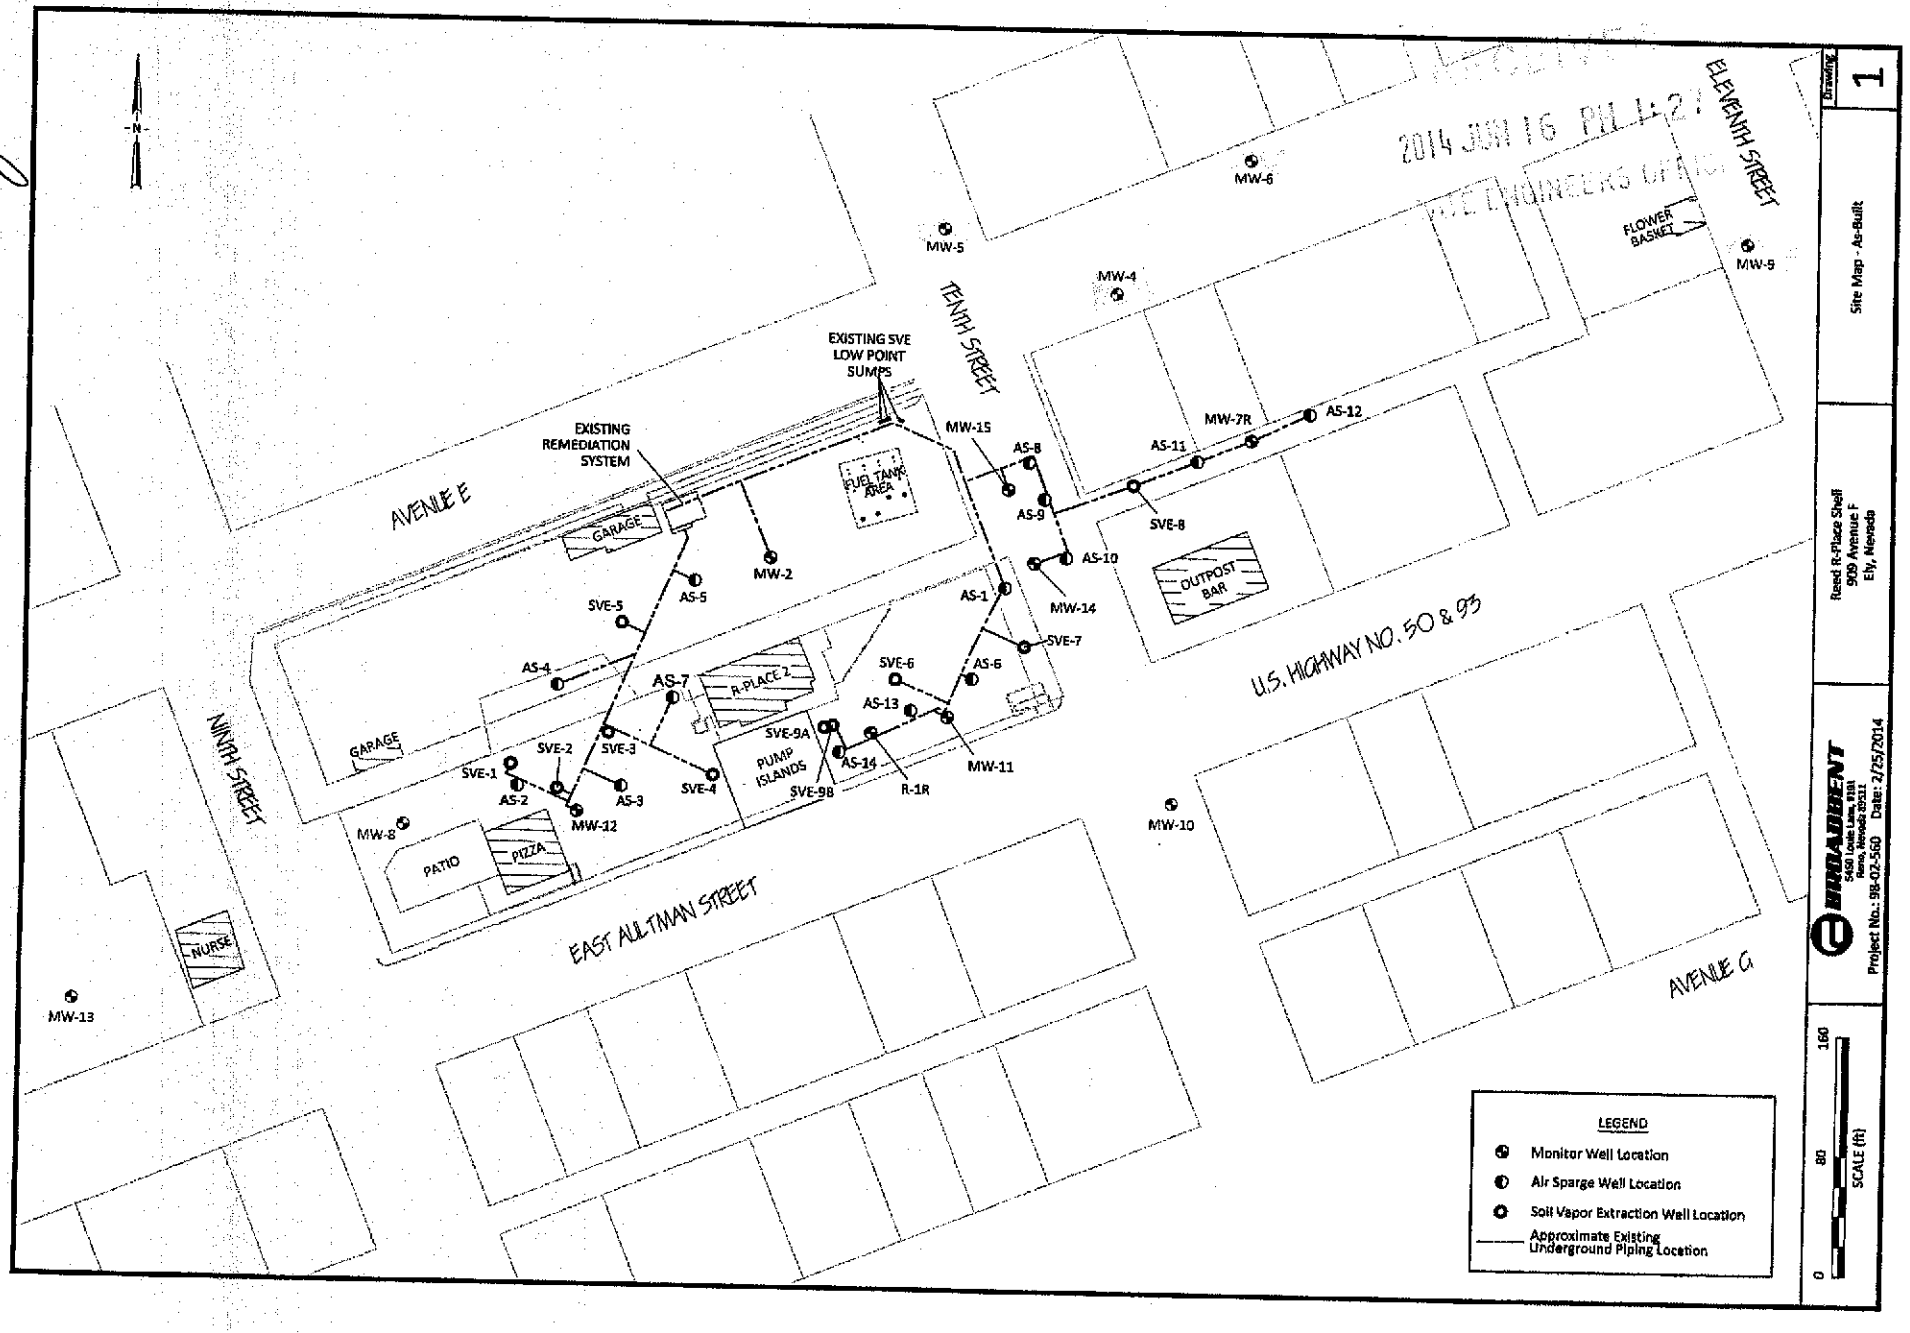

2014 JUN 16 PM 1:27
WRE ENGINEERS OFFICE
